

Water Main Replacement Project CIP No. 014

03 March 2021

Project Description

Construction of a new water transmission main to replace the old system. Construction includes installation of new water mains complete with service connections and all other apparatus to provide an operable pressurized water system conforming to AWWA Standards, requirements; abandonment and/or removal of existing water mains; installation of hydrants. A total of 13,700 lf of 8" PVC C900 with 314 1" MUNICIPEX Services in three areas in the City of El Monte. This is the first CIP Project of 2 in the same community.

Contractor

All Cities Engineering ACE

Construction Information


An action plan has been implemented and strict standards have been put in place to protect the construction workers as well as the community while working in the current COVID-19 environment. Construction crews are exercising appropriate physical distancing, wearing appropriate protective masks, and maintaining a safe and clean work area.

SAFETY IS THE PRIORITY! Please obey all Traffic and Pedestrian signs and encourage others to also do so. Always be aware that heavy construction equipment is operating in the area and take special care in driving in any and all construction areas.

Michael Baker International is providing Construction Management and Inspection for the project. For project information updates, for any questions or concerns please call 626.416.0095 You may leave a message and your call will be returned within 24 hours.

Construction improvement is Area 1, 2 & 3 are underway.

ACE has been working on installing the new 8" PVC water main line and setting services for the fire hydrants and 1" house connections

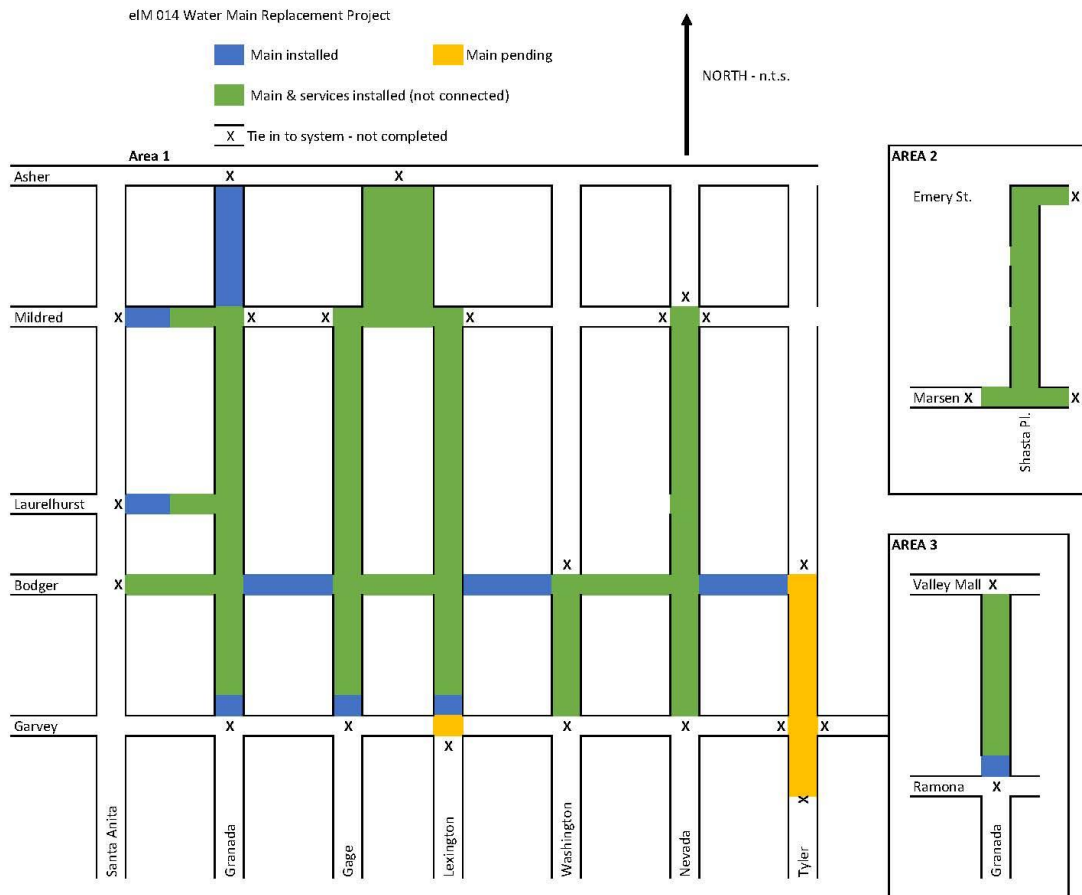

Backfill & compaction of services on Gage looking south from Bodger (Area 1)



Placing new curb & gutter on Granada looking south to Ramona (Area 3)



Tyler looking north from Garvey saw cutting prior to excavation (Area 1)



| Sunday | Monday | Tuesday | Wednesday | Thursday | Friday | Saturday |
|--------|--|---|---|---|--|----------|
| 28 | March 1 | 2 | 3 | 4 | 5 | 6 |
| | | <p>2 Week Look Ahead Schedule 0% Complete None</p> | | | | |
| | | <p>Week 1 : Possibly install main line on TylerFrom Bodger South, pour concrete on Granada and Ramona blvd, and install water services on Lexington Ave from Mildred Ave to Asher St. 0% Complete None</p> | | | | |
| | | | <p>Week 1 : Possibly construct slot patch on curb & gutter at Granada, install main line on Tyler and install water services on Granada from Mildred Ave to Asher St. 0% Complete None</p> | | | |
| | | | | <p>Week 1 : Install water service on Laurelhurst and install main line on Tyler St. 0% Complete None</p> | | |
| | | | | | <p>Week 1 : Install main line on Tyler Ave, install water services on Granada Ave from Bodger St to Garvey Ave 0% Complete None</p> | |
| 7 | 8 | 9 | 10 | 11 | 12 | 13 |
| | <p>Week 1 : Week 2 0% Complete None</p> | | | | | |
| | <p>Week 1 : Install water services on Bodger St. and install water main on Lexington across Garvey Ave 0% Complete None</p> | | | | | |



CITY OF EL MONTE
California

City of El Monte

Printed on Wed Mar 3, 2021 at 09:30 am PST

Job #: CIP 014 CIP 014 Water Main
11333 Valley Boulevard
El Monte, California 91731
5622437089

| | | | | | | | | |
|----|--|---|----|---|----|--|--|---|
| | | <p>Week 1 : Install water services on Midred St. and install main line on Lexington across Garvey Ave 0% Complete <i>None</i></p> | | <p>Week 1 : Possibly precision test on project area #2 and finish installing main line on Lexington 0% Complete <i>None</i></p> | | <p>Week 1 : Precision test project area #3 0% Complete <i>None</i></p> | | <p>Week 1 : Flush and chlorinate project area #2 and #3 0% Complete <i>None</i></p> |
| 14 | 15 | 16 | 17 | 18 | 19 | 20 | | |
| | <p>Week 1 : Week #3 0% Complete <i>None</i></p> | | | | | | | |
| | <p>Week 1 : Dechlorinate and sample day #1 at project area #2 and #3 0% Complete <i>None</i></p> | | | | | | | |
| | | <p>Week 1 : Sample day #2 at project area #2 and #3 0% Complete <i>None</i></p> | | | | | | |
| 21 | 22 | 23 | 24 | 25 | 26 | 27 | | |
| 28 | 29 | 30 | 31 | April 1 | 2 | 3 | | |

Key: Completed Tasks Task in Progress Critical Path
